I ran a delivery health check on a real engineering program.

Three MongoDB storage engine teams, 95 sprints, 2,943 public Jira tickets. Here is what the data says.

01 The headline numbers

02 Where predictability breaks

03 Where the time goes

04 The 90-day recovery plan

Swipe to start

THE HEADLINE

45%

of work committed at sprint start was done by sprint end.

01 **Only 16 of 84 sprints hit 80%**

The usual target for a predictable team.

02 **520 items were added mid-sprint**

On top of 772 that were committed.


03 **105 items sat in 3 or more sprints**

23 of them in 5 or more.

FINDING 1

More commitment, less delivery.


The Transactions team committed about 6 items a sprint in 2025 and 22 in 2026. Its say-do ratio fell from 59% to 39%.

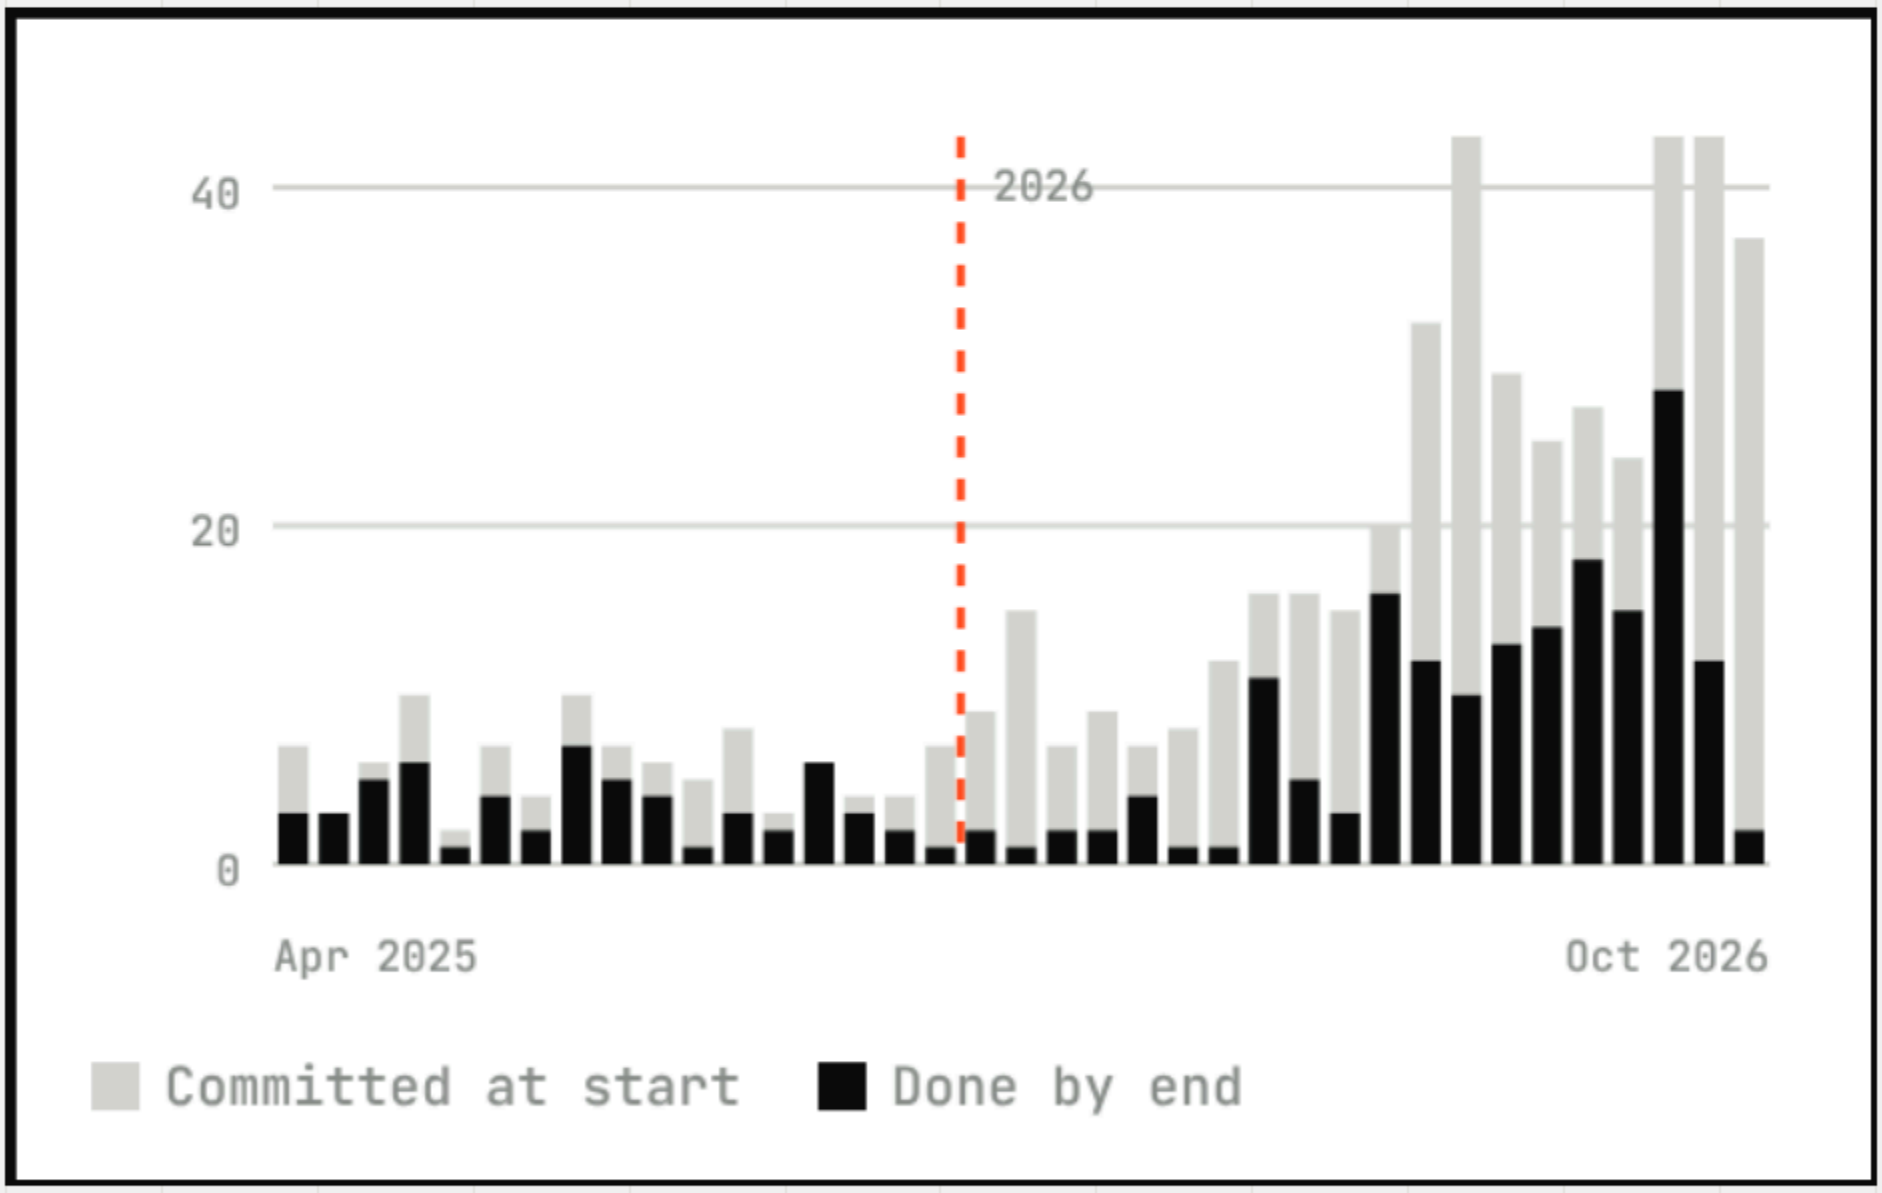

FINDING 2

Unplanned work is a standing load.


41% of items added mid-sprint were bugs or build failures. The plan held no capacity for them.

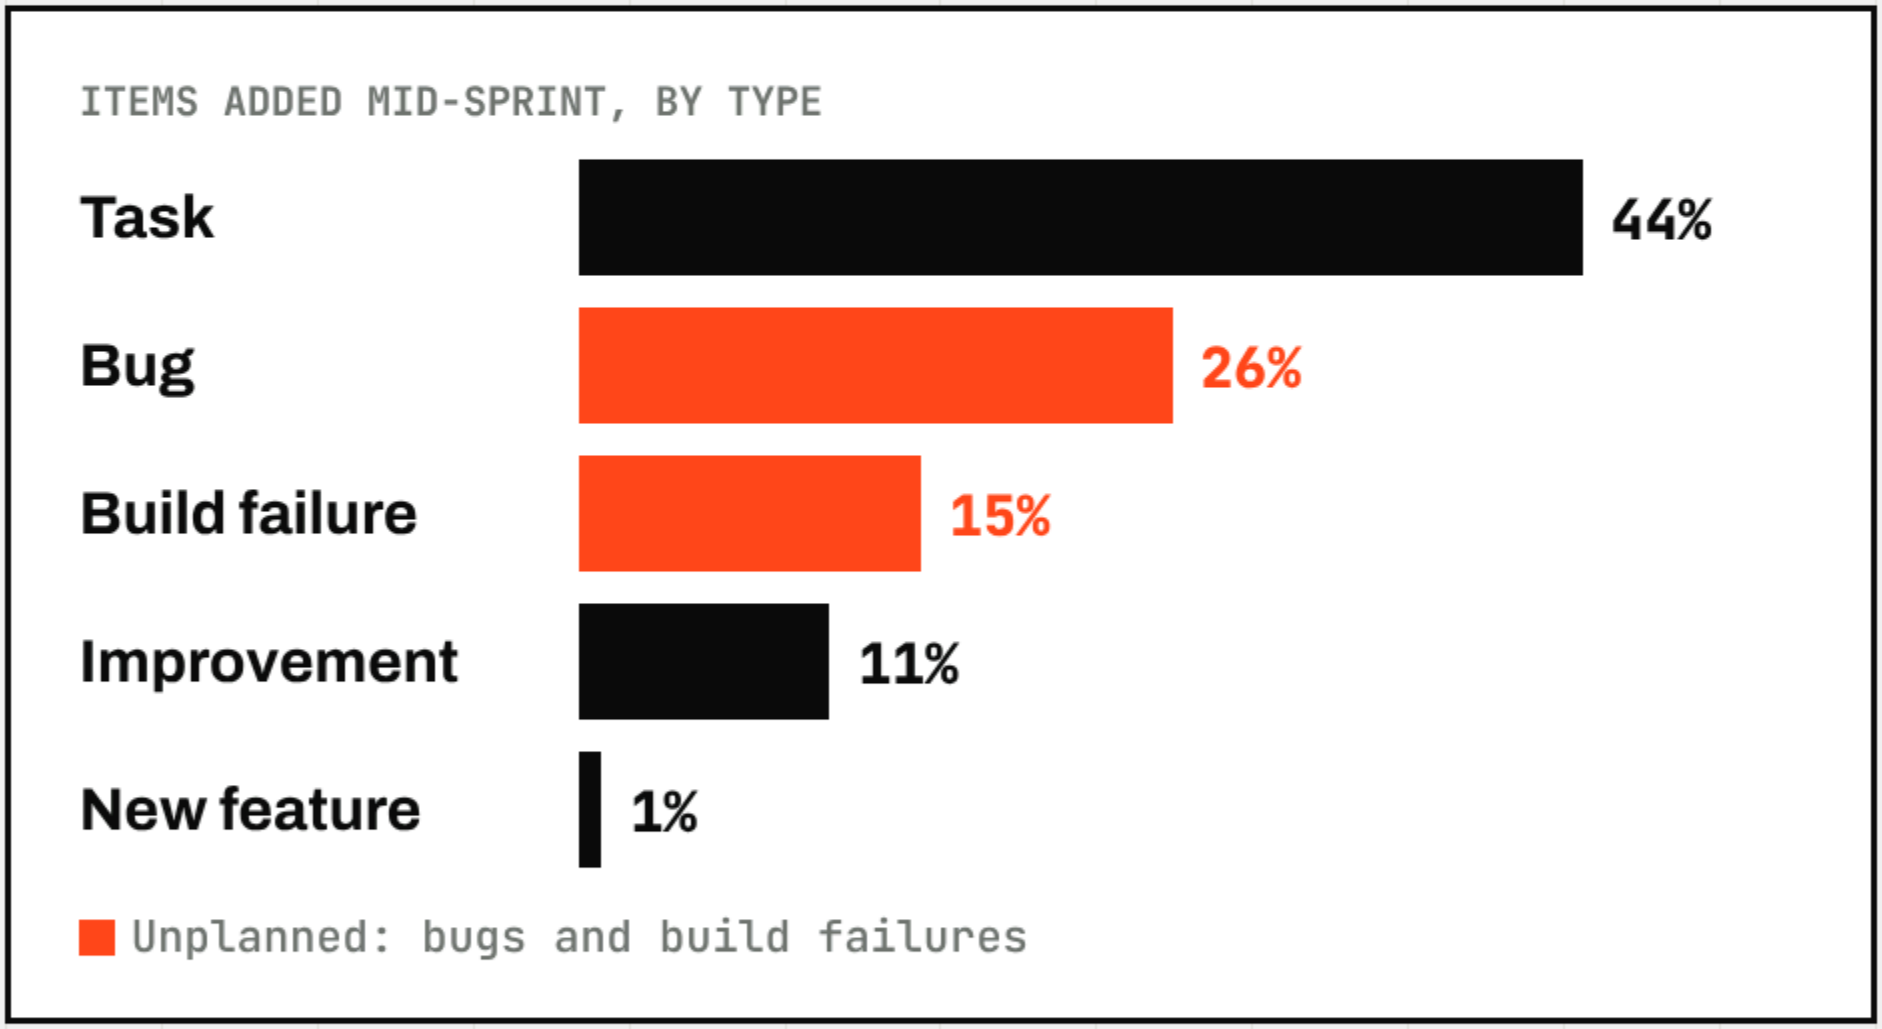

FINDING 3

Code review is the biggest queue.

Share of each team cycle time, from first start to done. 15% of reviewed items spent more than 7 days in review.

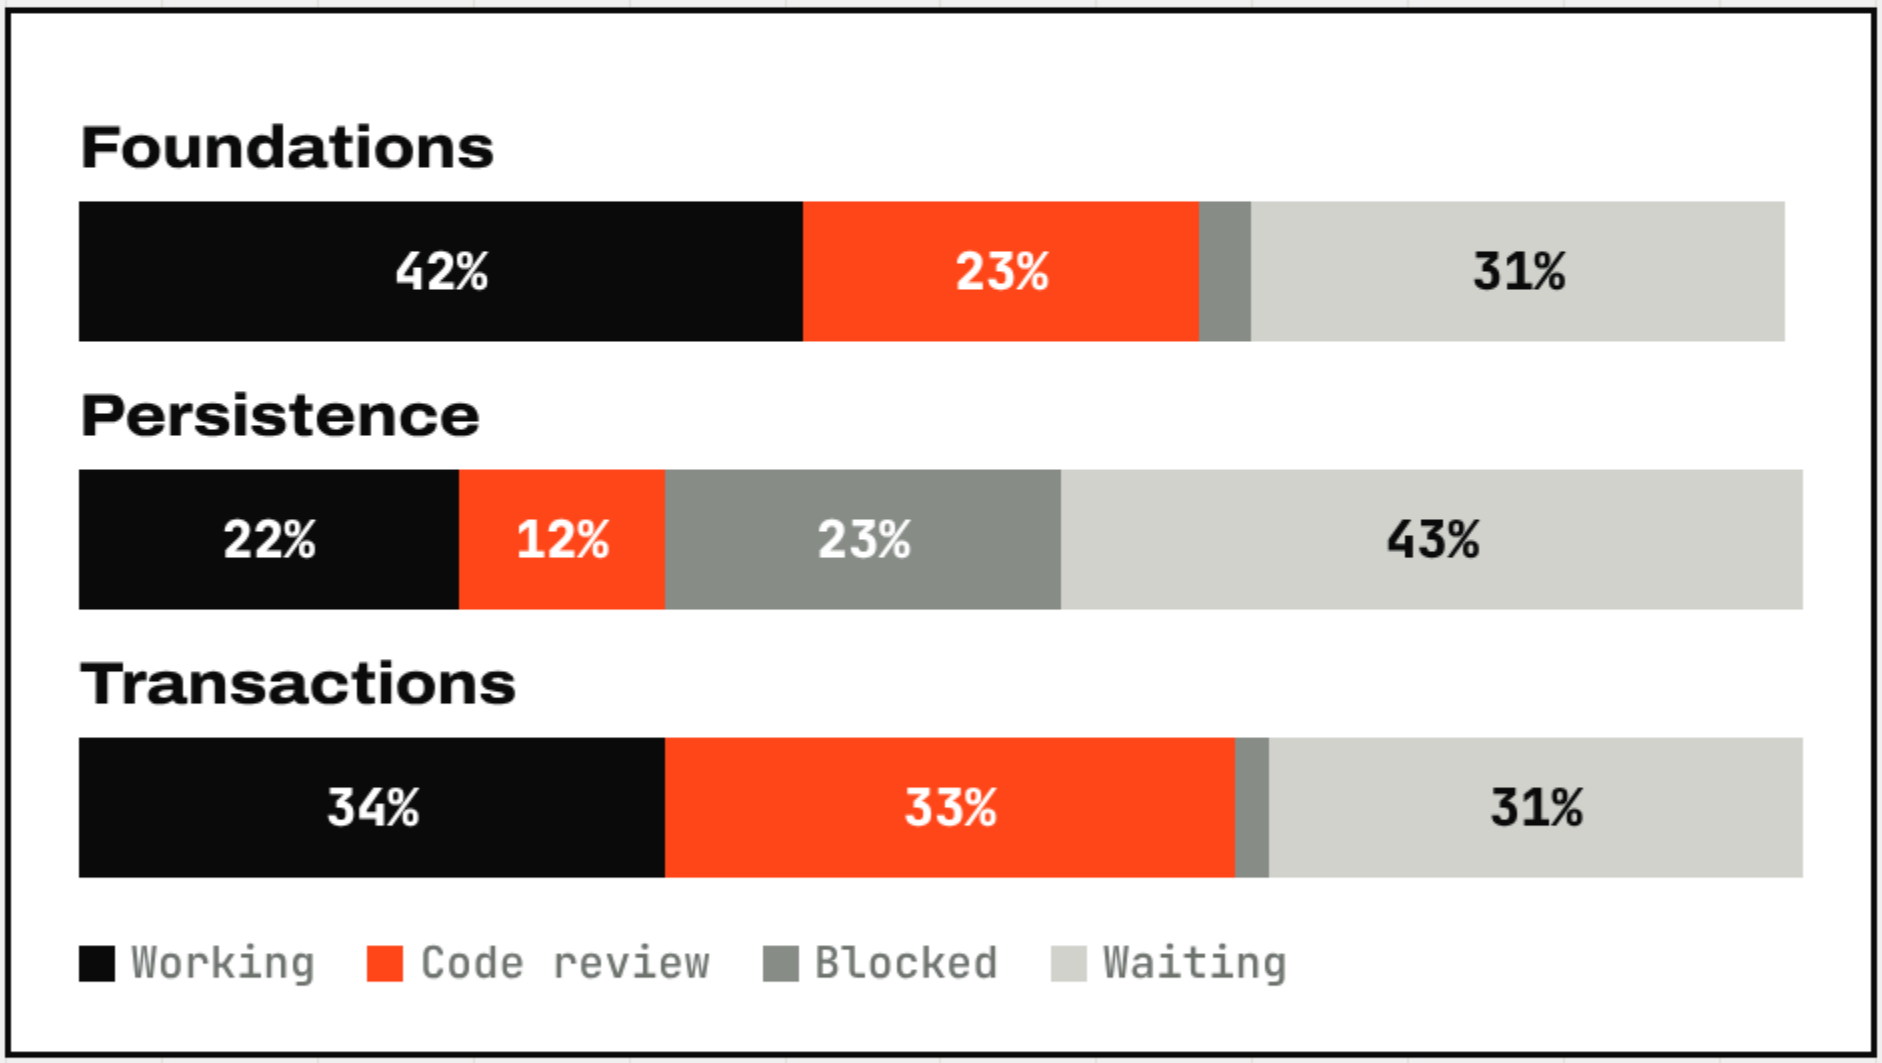

THE PLAN

What I would do in the first 90 days.

DAYS	ACTION	TARGET
1-30	Publish the dashboard, add a goal to every sprint, triage the 105 stuck items	Visibility
31-60	Commit to 80% of capacity, hold 20% for unplanned work, two-day review service level	Say-do 70%
61-90	Forecast from the 85th percentile, hand the metrics to the teams	Cycle time p85 under 12 days

YOUR TURN

What is your team say-do ratio?

The full report, Power BI file, Excel model and Python pipeline are on my GitHub. Link in the comments.

01 **Save it**

so it is there at your next planning session.

02 **Send it**

to the delivery manager or Scrum Master who needs it.

03 **Follow**

for the next field guide in the series.
